


STATEMENT OF WORK

Zoom Contact Center Professional Services

Prepared for Ionis Pharmaceuticals

August 14, 2026 · V6

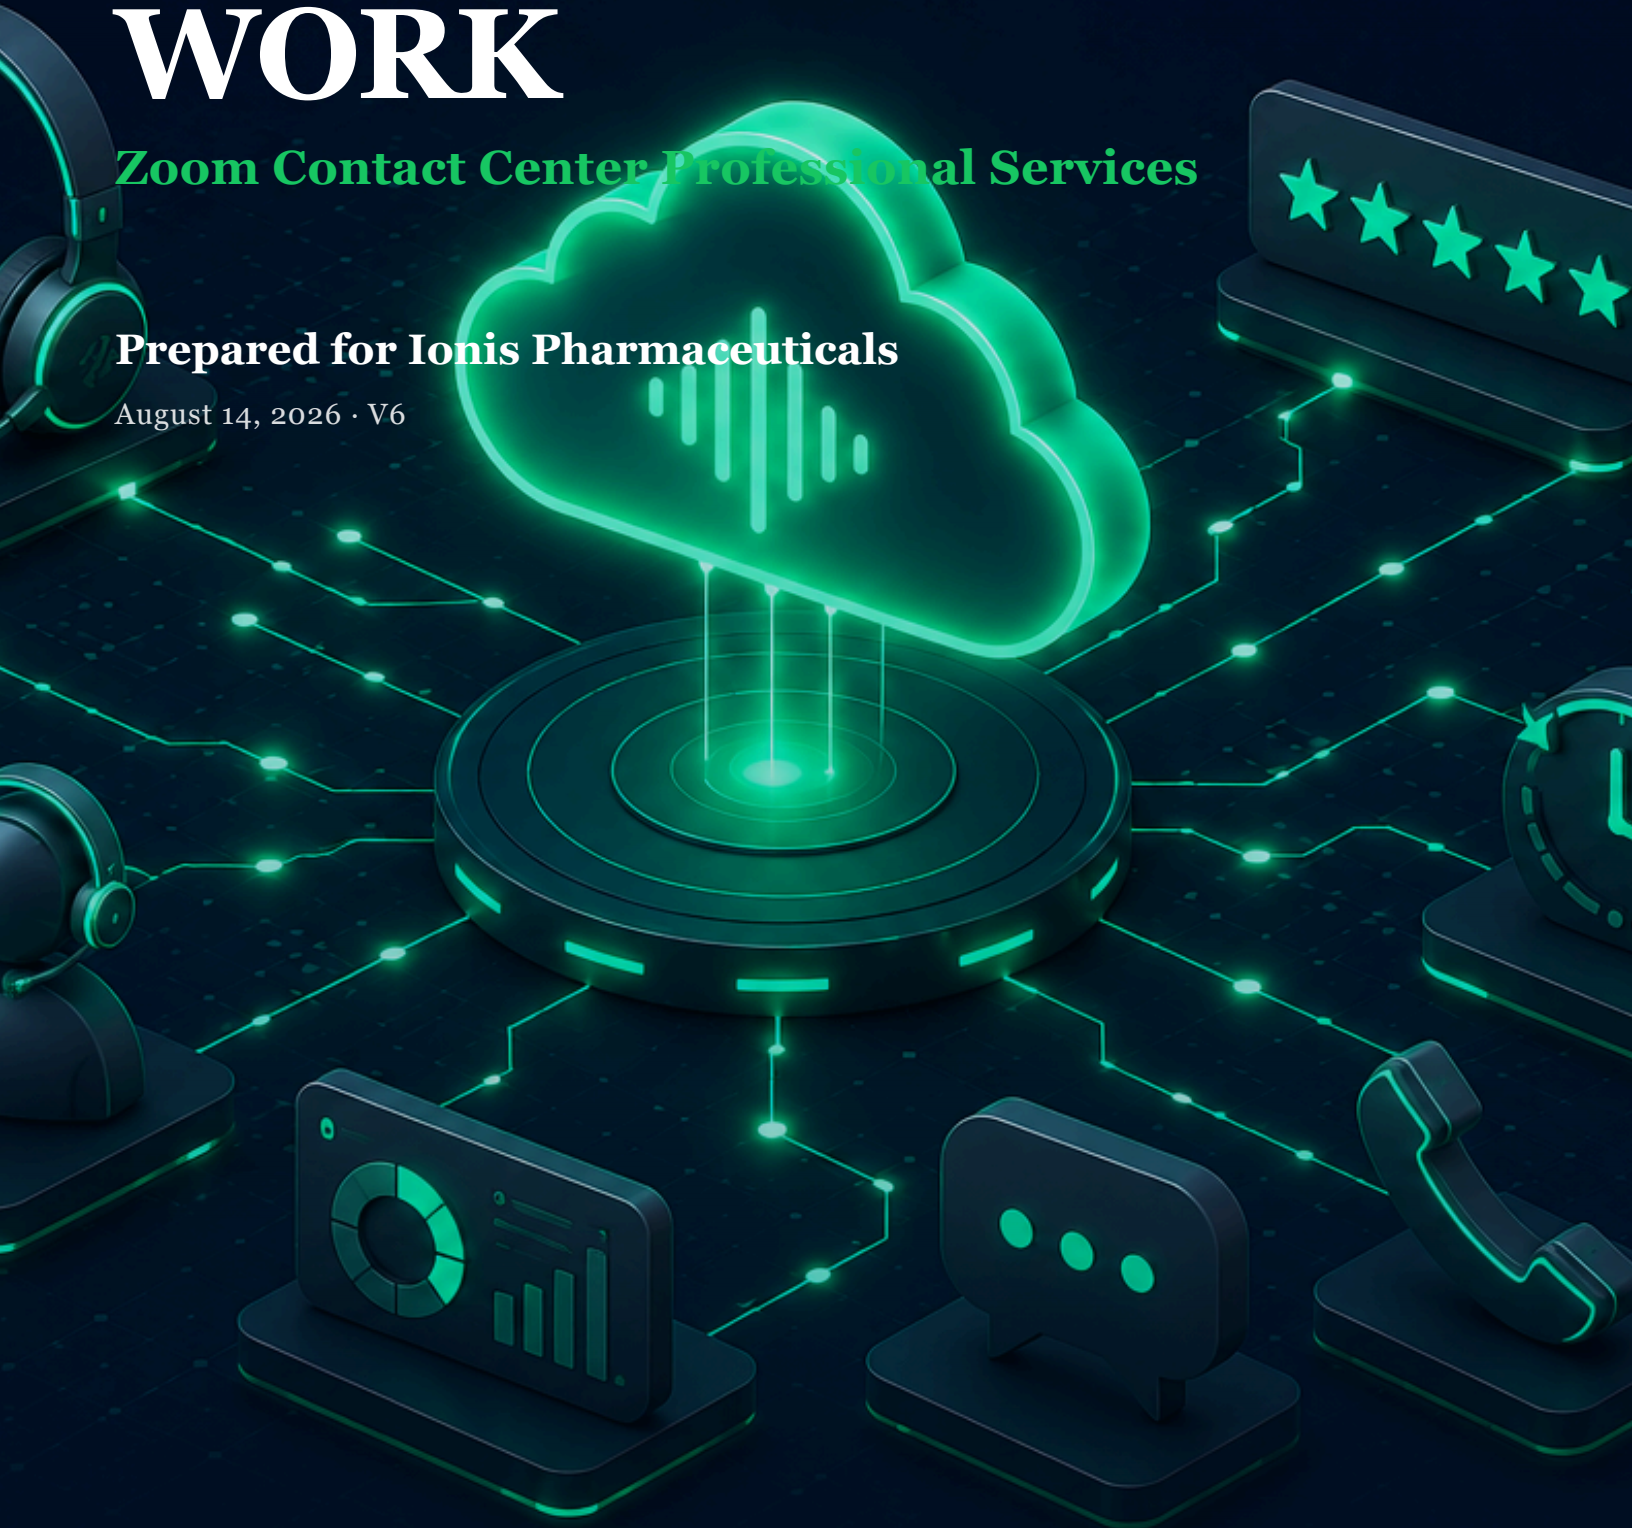

DOCUMENT CONTROL

PREPARED FOR	PREPARED BY
Ionis Pharmaceuticals	Packet Fusion, Inc. Ryan Dyla Solution Architect rdyla@packetfusion.com

SOW Number	V6
Issue Date	August 14, 2026
Project Reference	Zoom Contact Center Implementation – Ionis Pharmaceuticals
SOW Status	Final — Approved for Signature

REVISION HISTORY

Version	Date	Author	Description of Change
V1	August 13, 2026	Ryan Dyla	Initial SOW
V2	August 13, 2026	Ryan Dyla	
V3	August 14, 2026	Ryan Dyla	ZVA with voice
V4	August 14, 2026	Ryan Dyla	ZVA chat and voice + AI EA
V5	August 14, 2026	Ryan Dyla	ZVA Voice + AI EA
V6	August 14, 2026	Ryan Dyla	ZVA Voice + Chat + AI EA

Confidentiality Notice. This document contains confidential and proprietary information of Packet Fusion, Inc. and the Customer named above. It is provided solely for the purpose of evaluating and executing the services described herein and may not be reproduced, distributed, or disclosed to any third party without the prior written consent of Packet Fusion.

Executive Summary

Packet Fusion is pleased to partner with **Ionis Pharmaceuticals** (the "Customer") on the deployment of **Zoom Contact Center Professional Services**. This Statement of Work ("SOW") defines the services, deliverables, schedule, fees, and shared responsibilities for that engagement.

Our objective is a seamless cutover to the new platform — completed on schedule, with verified service quality, with users prepared to be productive on day one, and with a documented hand-off to Customer administrators for ongoing operation.

Engagement Snapshot

1 LOCATIONS	10 ZOOM CONTACT CENTER AGENTS	2 VIRTUAL AGENT WORKFLOWS	1 GO-LIVE EVENTS
-----------------------	--	--	----------------------------

Pricing Summary

Professional Services	\$26,000.00
Project Total	\$26,000.00

Optional services are listed in Section 9 and may be added by mutual written agreement.

1. Engagement Overview

1.1 About This SOW

This SOW is executed by Packet Fusion, Inc. ("Packet Fusion") and Ionis Pharmaceuticals (the "Customer") under, and is subject to, the Packet Fusion Master Services Agreement (the "MSA") executed between the parties. Capitalized terms used but not defined herein have the meanings given in the MSA. In the event of any conflict between this SOW and the MSA, the MSA controls except where this SOW expressly states otherwise.

1.2 Business Objectives

The Customer is engaging Packet Fusion to achieve the following outcomes:

- Consolidate communications on a single, cloud-delivered platform.
- Improve reliability and service quality through verified network readiness and a managed cutover.
- Reduce administrative overhead by standardizing call flows, user profiles, and policies.
- Enable hybrid and remote work with consistent communication experiences across locations.

- Provide a documented configuration and trained administrators capable of ongoing operation.

1.3 Scope at a Glance

Element	Quantity	Notes
Locations	1	Discrete physical sites in scope for cutover.
Zoom Contact Center agents	10	Agent licensing in scope; supervisor + admin profiles configured.
Virtual agent workflows	2	Enabled virtual-agent channels (voice / chat / SMS), each configured as its own workflow.
Queues, skills, and call flows	Per design	Validated against the legacy contact-center configuration where one exists.
Intent library	Per design	Trained intents drawn from the Customer's call-deflection priorities.
CRM / business-system integrations	Per design	Salesforce, HubSpot, Microsoft Dynamics, or equivalent — Customer provides API access.
Knowledge sources	Per design	Ingested knowledge bases / FAQ corpora the bot can reference.
Call recording configuration	Included	Retention windows and access permissions confirmed during design.
Channels (voice / chat)	Per design	Voice and chat channels enabled and validated.
Reporting + supervisor dashboards	Standard library	Customer-specific dashboards available as an optional service.
Fallback + escalation paths	Included	Live-agent handoff and after-hours fallback flows confirmed.
Go-Live events	1	One per site, sequenced per the agreed migration plan.
End-user training	Self-paced	Vendor video and knowledge-base library; instructor-led optional.
Administrative training	Included	Knowledge transfer to Customer system administrators.

2. Scope of Services

2.1 Delivery Methodology

Packet Fusion delivers cloud migrations using a PMI-aligned phased methodology. Each stage has defined activities, owners, and exit criteria; the project does not advance from one stage to the next

until exit criteria are met and confirmed in writing (email is acceptable). A typical engagement runs approximately 10–12 calendar weeks from project initiation through closure, with variation based on site count, number of DIDs in porting, and Customer readiness.

Stage	Name	When (relative to Go Live)	Purpose
1	Initiation	Project start	Establish team, internal assets, and the kickoff. Confirm scope, schedule, and tenant access.
2	Planning	6–8 weeks pre Go-Live	Assessment & design, E911, porting prep, training plan, and communications strategy.
3	Executing	4–5 weeks pre Go-Live	Submit porting, build and provision the tenant, coordinate training dates.
4	Monitoring / Controlling	2–3 weeks pre Go-Live	Confirm FOC, deploy hardware, execute UAT, obtain UAT sign-off.
5	Go Live / Production	1 week pre & Go-Live	Go/No-Go readiness, deliver training, run the Go-Live event, Day 1 support.
6	Closing	Post Go-Live	Cancel legacy services, lessons-learned, project closure, transition to CSM.

2.2 Stage 1 — Initiation

Packet Fusion assigns a dedicated Project Manager (PM) and Implementation Engineer (IE) and establishes the working environment for the project before the customer-facing kickoff.

2.2.1 Resource assignment.

- Assign Packet Fusion Project Manager (PM) as Customer's single point of contact.
- Assign Packet Fusion Implementation Engineer (IE) responsible for technical delivery.

2.2.2 Project workspace.

Packet Fusion uses its Cloud Connect portal as the single workspace for project artifacts, documents, and ongoing collaboration with the Customer team.

- Cloud Connect project workspace provisioned for the engagement; access invitations sent to the Customer Project Manager, Technical Lead, and authorized signer.
- Document workspace (SharePoint folder, surfaced inside Cloud Connect) created for SOWs, workbooks, network test results, and design artifacts.
- Contract and SOW reviewed by the assigned PM.

2.2.3 Kickoff.

- Customer kickoff: scheduled within five (5) business days of project assignment. PM delivers the kickoff deck, an AI-generated meeting summary is shared, recurring cadence meetings are

scheduled, and the first technical session is calendared.

- Packet Fusion admin profile confirmed in the Customer's tenant.
- On request post-kickoff, a shared chat channel can be established between the Packet Fusion project team and the Customer team for day-to-day collaboration outside of scheduled meetings.

2.3 Stage 2 — Planning

Planning typically begins 6–8 weeks before the target Go-Live date. UCaaS and Contact Center work streams run in parallel — Voice infrastructure, Emergency Services, and Porting on the UCaaS side; Queue / Flow / Skill design and CRM integrations on the Contact Center side.

2.3.1 Queue, Flow, and Skill Design

- Inventory the legacy contact-center configuration (queues, IVR menus, after-hours / holiday hours, skill assignments) where one exists.
- Design call queues with target service levels and overflow / fallback rules.
- Design IVR / call flows with menu options, business-hours logic, and exception paths.
- Design skill-based routing and agent groups.
- Customer signs off on the queue / flow / skill design before tenant build begins.

2.3.2 Bot Persona + Conversation Design

- Confirm the use cases the virtual agent should handle (top deflection candidates).
- Design the bot persona — name, voice, tone, fallback language.
- Map the conversation tree for each use case, including disambiguation and confirmation prompts.
- Identify live-agent handoff triggers and the queues that receive transferred conversations.

2.3.3 CRM + Business-System Integrations

- Identify CRM(s) in scope (Salesforce, HubSpot, Microsoft Dynamics, Zendesk, ServiceNow, etc.).
- Confirm API access, OAuth scopes, and data mapping (contact lookup, screen pops, activity logging).
- Identify WFM / QM integrations if separately licensed.
- Document the integration design and sequence integration work in the Executing stage.

2.3.4 Knowledge Sources + Intent Library

- Identify the knowledge bases / FAQs / corpora to ingest.
- Confirm refresh cadence and ownership for each source.
- Inventory candidate intents drawn from historical call / chat reasons.
- Define language coverage and the fallback when an unsupported language is detected.

2.3.5 Call Recording + Retention

- Confirm recording scope (always-on, on-demand, agent-pause), retention windows, and access permissions.
- Confirm any PCI / PII redaction requirements and the rules that drive pause-and-resume.

- Document storage destination (vendor cloud vs. customer-provided) and access controls.

2.3.6 Training Planning

- Confirm end-user / agent training count and audience.
- Confirm administrator training plan.

2.3.7 Change Management & End-User Enablement

Packet Fusion helps the Customer drive adoption with a light-weight change-management approach focused on user readiness, not just compliance comms.

- Joint review of the Customer's change-management approach (stakeholders, audiences, key messages, training plan).
- End-user / agent communication templates provided (pre-cutover save-the-date, what-to-expect, training links, day-of cheatsheet); the Customer adapts and sends them under their brand.
- Self-paced training resource library curated for the Customer's audience mix; Customer Champions / IT identified for first-line questions.
- Optional instructor-led training sessions are scoped under Section 2.8 if the Customer wants live coverage in addition to self-paced resources.

2.4 Stage 3 — Executing

Executing runs the UCaaS port-and-provision flow in parallel with the Contact Center tenant build. Training is coordinated for end users, agents, and supervisors.

2.4.1 Tenant Build

- Build queues, IVR / call flows, and skill assignments per the validated design.
- Configure business hours, holiday calendars, and overflow routing rules.
- Assign agent licenses, supervisor profiles, and admin roles.
- Apply call-recording configuration including any pause-and-resume rules.

2.4.2 Bot Build + Intent Training

- Build the bot persona(s) per the Planning-stage design.
- Ingest the knowledge sources and train the intent library.
- Wire voice and chat channels and confirm grammars / NLU coverage.
- Build live-agent handoff to the agreed queues.

2.4.3 Integrations

- Build the in-scope CRM integration(s) per the Planning-stage design.
- Validate screen pops, contact lookups, and activity logging end-to-end.
- Build WFM / QM integrations where in scope.
- Configure SSO and SCIM / directory synchronization.

2.4.4 Training Coordination

- Packet Fusion PM coordinates training schedule with the Packet Fusion Trainer.
- Customer finalizes training dates.

2.5 Stage 4 — Monitoring / Controlling

User Acceptance Testing is executed and signed off prior to Go-Live. Outstanding configuration issues are remediated and re-tested in the same window.

2.5.1 Communications

- Customer sends user / agent communications confirming the cutover date.

2.5.2 Contact Center UAT

- Packet Fusion provides UAT test form covering queue routing, IVR menus, skill assignment, business-hours logic, recording capture, and CRM screen pops.
- Customer executes UAT with representative agent + supervisor users.
- Packet Fusion and Customer review UAT results together; Packet Fusion makes modifications as needed.
- Customer signs off on UAT prior to Go-Live.

2.5.3 Intent Validation + NLP Testing

- Run test conversations covering the in-scope use cases on voice and chat channels.
- Customer reviews intent coverage and disambiguation behavior.
- Packet Fusion tunes intent boundaries, phrasing, and fallback triggers.
- Customer signs off on the intent library prior to Go-Live.

2.6 Stage 5 — Go Live / Production

Go/No-Go readiness review, training delivery, the Go-Live event, and Day 1 support.

2.6.1 Go/No-Go Readiness

- Determine readiness for Go-Live, including Tier 1 Support readiness on the Customer side.
- Packet Fusion Trainer delivers end-user / agent training.
- Packet Fusion IE delivers administrator training.

2.6.2 Go-Live Event

- Packet Fusion and Customer follow the Go-Live test plan and record results.
- Packet Fusion provides Day 1 Support during the cutover window.

2.6.3 Change Management & Day 1 Support

- Customer sends the Go-Live announcement using the template provided in Planning, with day-one cheatsheet and support contact info.
- Packet Fusion provides Day 1 floor-walking guidance (remote) and escalation paths for issues that surface during the cutover window.
- Customer Champions / IT first-line owners pre-briefed on common Day 1 questions.

2.7 Stage 6 — Closing

Project closing wraps up legacy decommissioning, captures lessons learned, and transitions to the Customer's Customer Success Manager (CSM) for ongoing engagement.

- Customer requests cancellation of old cloud services (if applicable).
- Customer requests cancellation of telco services (if applicable).
- Packet Fusion PM hosts the lessons-learned call and project closure meeting.
- Project transitions to the Customer Success Manager (CSM) for ongoing engagement and any future change orders.

2.8 Training Services

Included. Self-paced agent training via Zoom's video library and knowledge base; instructor-led administrator + supervisor training delivered by Packet Fusion.

Optional. Live, remote, instructor-led agent training sessions (up to 20 attendees per session). See Section 9.2 for pricing.

2.9 Engineering & Integration Services

The following services are included if explicitly indicated in the Scope at a Glance (Section 1.3) or added via change order:

- CRM integration (Salesforce, HubSpot, Microsoft Dynamics, Zendesk, ServiceNow, or equivalent) — screen pop, contact lookup, activity logging.
- Knowledge-source ingestion — connectors to FAQ / KB sources with refresh cadence.
- Workforce Management (WFM) integration — schedule adherence, forecasting, and intraday data exchange.
- Intent training — iterative tuning against a corpus of representative utterances.
- Quality Management (QM) integration — recording handoff, calibration workflow, and scorecard sync.
- Voice + chat channel wiring — IVR overlay, web chat widget, mobile SDK integration where in scope.
- Custom IVR / call-flow design for complex menus, after-hours routing, and queue overflow logic.
- Live-agent handoff — queue + context-transfer configuration.
- Single Sign-On (SSO) and SCIM directory sync for agents, supervisors, and admins.
- CRM context API — surface caller / chat context for downstream review.

2.10 Optional Services

The following services are not included in the base scope and may be added by mutual written agreement. Pricing is summarized in Section 9.2.

- Custom reporting / supervisor dashboards beyond the standard library.
- Bot persona localization — additional language coverage beyond the in-scope set.

- Workforce Optimization (WFO) suite integration — recording, evaluation, coaching workflow handoff.
- Conversation flow optimization — A/B testing of intent paths and fallback rules.
- Additional live, instructor-led remote training sessions.

3. Deliverables

The following deliverables will be produced under this SOW. Each deliverable is subject to the acceptance process described in Section 11.

#	Deliverable	Format	Acceptance Criteria
D1	Project Plan & RAID Log	Smartsheet / PDF	Plan reflects scope, milestones, owners, and dependencies; reviewed and acknowledged in writing by Customer PM.
D2	Implementation Workbook	Excel	All users, sites, configuration, and feature assignments populated and approved by Customer authorized signer.
D3	Queue, Flow & Skill Design Package	PDF / Visio	All in-scope queues, IVR / call flows, skill assignments, and routing rules depicted; approved by Customer authorized signer.
D4	Bot Persona + Conversation Design	PDF	Persona, voice, conversation tree, disambiguation prompts, and fallback flows approved by Customer authorized signer.
D5	CRM Integration Design	PDF	Documents the API integration design — screen pop fields, contact-lookup keys, activity-logging template; approved by Customer authorized signer.
D6	Intent Library	Platform export	Trained intents covering the in-scope use cases; signed off by Customer reviewer.
D7	Network Readiness Review	PDF + test screenshots	Customer runs the platform's network-readiness test at each in-scope site and submits results to Packet Fusion. Packet Fusion documents findings, identified risks, and remediation owners; Customer acknowledges remediation responsibilities.
D8	UAT Plan & Results	PDF / Excel	All planned test cases executed; pass/fail results recorded; Customer authorized signer accepts UAT results.
D9	Go-Live Confirmation	Sign-off form	Cutover confirmed by Customer site lead; outstanding items captured for Day 1 Support follow-up.
D10	Final Solution Design Report	PDF	Documents as-built configuration, integrations, and admin procedures; delivered at or before project closure.

#	Deliverable	Format	Acceptance Criteria
D11	Administrator Knowledge Transfer	Live session + recording	Recorded session covers admin portal, user / agent lifecycle, configuration edits, and reporting; Customer acknowledges completion.
D12	Project Closure Memo	PDF	Confirms project closure and CSM transition, and lists any deferred items for future change orders.

4. Out of Scope

The following are explicitly out of scope for this SOW. They may be added by change order under Section 10 if the Customer wishes Packet Fusion to perform them.

- Design, procurement, configuration, or remediation of Customer LAN/WAN infrastructure.
- Quality of Service (QoS) policy design or configuration on Customer network equipment.
- Firewall, ACL, or NAT/SBC configuration on Customer-owned network equipment.
- Power over Ethernet (PoE) port activation or configuration.
- Installation or configuration of software on Customer end-user PCs or mobile devices.
- Customization of individual user endpoints or phone settings beyond the standard profile.
- Decommissioning, removal, or disposal of legacy equipment or services.
- Configuration, diagnostics, or troubleshooting of the Customer's legacy premise PBX.
- Re-flashing of existing phones or configuration of redirect URL via DHCP.
- Unboxing, placement, or physical installation of new phones (available as an Optional service).
- Customer mobile-device management (MDM) configuration, diagnostics, or troubleshooting.
- Recording, production, or sourcing of greeting prompts, hold music, or IVR audio.
- Contact center (Zoom Contact Center, Five9, Genesys, etc.) design or implementation unless explicitly listed in Section 1.3.
- Data migration from legacy voicemail, call recording, or analytics systems.
- Procurement of CSRs from the Customer's existing carrier(s).

5. Assumptions

This SOW, including the schedule and fees, is based on the following assumptions. A material change to any assumption may require a change order under Section 10.

- The Customer has an active vendor tenant (or will procure one) sized appropriately for the in-scope users, with administrative access available to Packet Fusion under a documented account.
- The Customer's network meets the vendor's published bandwidth, jitter, latency, and packet-loss recommendations at each in-scope location, or remediation will be completed by the Customer in

advance of cutover.

- The Customer will make available a designated Project Manager, Technical Lead, and an authorized signer with decision-making authority throughout the engagement.
- Services are delivered remotely Monday–Friday during U.S. business hours (8:00 AM – 6:00 PM Pacific) unless explicitly stated otherwise. Cutover support may extend outside business hours by mutual agreement.
- Number porting timelines are subject to the losing carrier's acceptance and FOC scheduling, which are outside Packet Fusion's control.
- All required Customer-provided inputs (workbook entries, prompts, LOAs, CSRs, SSO metadata) will be returned to Packet Fusion within five (5) business days of request.
- Existing premise systems remain the responsibility of the Customer and their incumbent vendor throughout migration. Packet Fusion is not responsible for legacy PBX issues that surface during peering or cutover.
- The work in this SOW is performed under the master pricing and terms in effect as of the SOW Issue Date.

6. Customer Responsibilities

The Customer is responsible for the following throughout the engagement. Delays in any of these items may impact the project schedule and may trigger a change order.

6.1 Engagement & Governance

- Identify and make available a Customer Project Manager, Technical Lead, Site Lead per location, and an authorized signer.
- Attend scheduled meetings and respond to Packet Fusion requests within the agreed turnaround times.
- Approve or reject deliverables in writing within five (5) business days of delivery.

6.2 Network & Infrastructure

- Provide and maintain LAN/WAN, Wi-Fi, firewall, and Internet connectivity meeting the vendor's published requirements.
- Implement remediation recommended in the Network Readiness Review prior to cutover.
- Configure firewalls, ACLs, NAT/SBC, and QoS to support the vendor's voice and video traffic.
- Provide PoE port activation and switch capacity for any in-scope physical devices.

6.3 Data & Inputs

- Procure Customer Service Records (CSRs) from the existing carrier(s) for all locations and accounts requiring porting services.

- Provide service addresses, authorized contacts, and Billing Telephone Number (BTN) for each phone bill / carrier account.
- Supply Letters of Authorization (LOAs) signed by an authorized signer for each port order.
- Provide accurate Registered E911 Address and location information for each user and device.
- Supply pre-recorded greetings, IVR prompts, and hold-music files in the formats required by the vendor.
- Provide SSO metadata (IdP) and any directory-sync configuration.
- Assemble and validate data exported from legacy systems (voicemail, recordings, analytics).

6.4 Premise & Endpoints

- Manage all Customer-side premise PBX configuration, diagnostics, and troubleshooting.
- Unbox, physically place, and cable any new IP phones (unless On-site Deployment is purchased as an Optional service).
- Manage Customer mobile-device configuration, diagnostics, and troubleshooting.
- Decommission and dispose of legacy equipment after project closure.

7. Timeline & Milestones

Anticipated go-live: **October 15, 2026**. This is the only date Packet Fusion commits to under this SOW; week-range estimates below are illustrative.

This engagement is sized for approximately **10 weeks** from project initiation to closure. The week ranges below are typical stage distribution; specific dates are finalized in the project plan produced during Planning, based on porting Firm Order Commitments (FOCs) and Customer site readiness.

Stage	Relative Weeks
Initiation & Kickoff	Week 1
Planning — Assessment, Design, Porting Prep	Weeks 1–4
Executing — Tenant Build & Porting Submission	Weeks 4–7
Monitoring / Controlling — UAT & Hardware	Weeks 7–9
Go-Live & Day 1 Support	Week 10
Closure & CSM Transition	Week 11

Week 1 begins at SOW execution. Durations are working weeks and exclude federal holidays and Customer-declared blackout windows.

8. Pricing & Payment Schedule

8.1 Fee Summary

Service	Type	Fee
Zoom Contact Center Professional Services (base scope per Section 2)	Fixed Fee	\$26,000.00
Project Total		\$26,000.00

8.2 Optional Services

Optional Service	Unit	Fee
Additional CRM integration build beyond the in-scope system	Per integration	By quote
Custom reporting / supervisor dashboard build	Per dashboard	By quote
Live remote instructor-led training session (up to 20 attendees per session)	Per session	\$290.00

Optional services are added by mutual written agreement (email accepted) and invoiced upon completion of the optional engagement, unless otherwise stated.

8.3 Invoicing Milestones

Where fees are billable, Packet Fusion will invoice against the following milestones. Invoices are net 30 from issue date unless the MSA states otherwise.

Trigger	Percent	Amount
SOW Execution	50%	Per Section 8.1
Go-Live and Customer acceptance	50%	Per Section 8.1

8.4 Expenses

All services are delivered remotely unless otherwise stated. Any pre-approved travel will be invoiced at cost per the MSA travel & expense policy.

8.5 Taxes

All fees are exclusive of applicable sales, use, and similar transaction taxes. The Customer is responsible for any such taxes other than taxes based on Packet Fusion's net income.

9. Change Management

Changes to scope, schedule, fees, deliverables, or assumptions require a written Change Order signed by both parties before work on the change commences. The process is intentionally lightweight but explicit:

Step 1 — Request. Either party submits a written change request to the other party's Project Manager describing the change and the reason for it.

Step 2 — Impact Assessment. Within five (5) business days, Packet Fusion will assess the impact on scope, schedule, fees, deliverables, and assumptions, and provide a written Change Order for the Customer's review.

Step 3 — Approval. The Change Order takes effect when signed by the authorized signers of both parties. Until then, the original SOW remains in force and the project schedule continues to count the impact-assessment time against the affected milestones.

Step 4 — Execution. Packet Fusion incorporates the approved change into the project plan and tracks it through the normal status-reporting cadence.

Customer-caused delay. Delays in performance or delivery caused by the Customer — including without limitation delays in completing the implementation workbook, approving the call-flow design, supplying LOAs/CSRs, or remediating network findings — may result in schedule adjustment and/or additional fees, processed through this same change-order procedure.

10. Acceptance Process

10.1 Deliverable Acceptance

For each deliverable listed in Section 3, the following process applies:

- Packet Fusion submits the deliverable to the Customer's designated reviewer in writing (email is acceptable).
- The Customer reviews against the stated acceptance criteria within five (5) business days.
- If accepted, the Customer authorized signer confirms acceptance in writing.
- If rejected, the Customer provides a written list of specific, defensible deficiencies referencing the acceptance criteria. Packet Fusion remedies the deficiencies and resubmits.
- If the Customer does not respond within five (5) business days, the deliverable is deemed accepted.

10.2 Site Go-Live Acceptance

Each site is deemed accepted at Go-Live when: (a) ported numbers complete; (b) test calls succeed in both directions; (c) E911 returns correct location data; and (d) the Customer site lead signs off on the cutover form. Outstanding cosmetic items are captured for Day 1 Support follow-up.

10.3 Project Closure

The project is closed when: (a) all deliverables in Section 3 have been accepted; (b) all sites have completed Day 1 Support; and (c) the Project Closure Memo is signed by both PMs. Any open items at closure are deferred to a future change order or to the Customer's ongoing support relationship.

11. Terms & References

11.1 Master Services Agreement

This SOW is governed by the Packet Fusion Master Services Agreement (the "MSA") executed between the parties and incorporated here by reference. The MSA controls all terms not expressly modified by this SOW, including confidentiality, intellectual property, warranty, indemnification, limitation of liability, term and termination, and governing law.

11.2 Confidentiality

Each party will protect the Confidential Information of the other party as required by the MSA. Project deliverables produced under this SOW are considered Confidential Information of the Customer except for Packet Fusion's pre-existing methodologies, templates, and know-how, which remain the property of Packet Fusion.

11.3 Data Handling

Packet Fusion will access only the Customer data and systems necessary to deliver the services in this SOW. Any Customer data received will be handled per the MSA and applicable privacy laws. The Customer is responsible for ensuring its vendor tenant and downstream integrations comply with its own regulatory requirements (e.g., HIPAA for covered entities).

11.4 Order of Precedence

In the event of a conflict between documents, the order of precedence is: (1) the MSA; (2) any signed Change Order to this SOW; (3) this SOW; (4) any attached appendices.

11.5 Entire Agreement

This SOW, together with the MSA and any signed Change Orders, constitutes the entire agreement of the parties with respect to its subject matter and supersedes all prior or contemporaneous communications, representations, or agreements, whether oral or written, relating to that subject matter.

12. Authorization & Signature

By signing below, each party agrees to the terms of this Statement of Work and authorizes Packet Fusion to proceed with the services described herein.

PACKET FUSION, INC.

Authorized Signature

Name & Title

Date

IONIS PHARMACEUTICALS

Authorized Signature

Name & Title

Date
